


**CITY OF KEO, ARKANSAS**  
**2ND STREET SEWER IMPROVEMENTS**

**BID PROPOSAL**

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
1	1	L.S.	Mobilization including preparatory work and operations, including but not limited to, movement of personnel, equipment, supplies, and incidentals to the project site for the lump sum price of  _____ Dollars and _____ Cents/L.S	\$ _____	\$ _____
2	3	E.A.	Demolition and removal of existing manholes and all associated appurtenances following all applicable ADEQ and ADH guidelines for the removal of manholes for the unit price of  _____ Dollars and _____ Cents/EA	\$ _____	\$ _____


BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
3	520	L.F.	Abandonment of existing sewer main and all associated appurtenances following all applicable ADEQ and ADH guidelines for the removal of sewer main for the unit price of	\$ _____	\$ _____
			_____ Dollars and Cents/L.F.		
4	200	S.Y.	Removal of existing asphalt pavement to neat lines for the unit price of	\$ _____	\$ _____
			_____ Dollars and Cents/S.Y.		

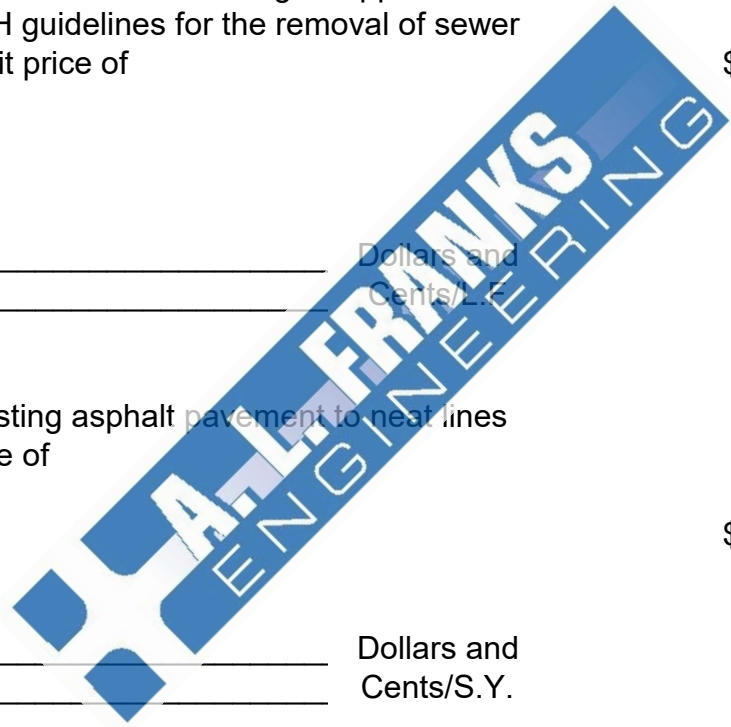


BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
5	1	L.S.	Perform removal and replacement of existing stormdrain culverts of various sizes and materials on positive grade including all labor, materials, grading and compaction and as shown in the plans and specifications for the lump sum price of  _____ Dollars and _____ Cents/L.S.	\$ _____	\$ _____
6	200	S.Y.	Provide and install asphalt pavement repair as shown in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/S.Y.	\$ _____	\$ _____

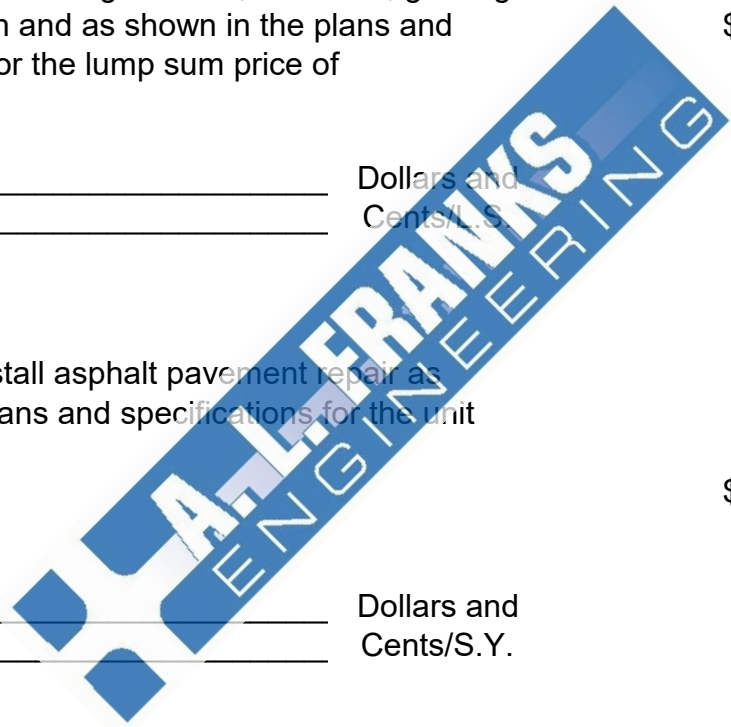

BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
7	200	L.F.	Provide and install 8" SDR-26 gravity sewer main by open cut including, bedding, all materials, labor and equipment as required in accordance with the plans and specifications for the unit price of  _____ Dollars and _____ Cents/L.F.	\$ _____	\$ _____
8	320	L.F.	Provide and install 8" SDR-21 gravity sewer main by bore including all materials, labor and equipment as required in accordance with the plans and specifications for the unit price of  _____ Dollars and _____ Cents/L.F.	\$ _____	\$ _____

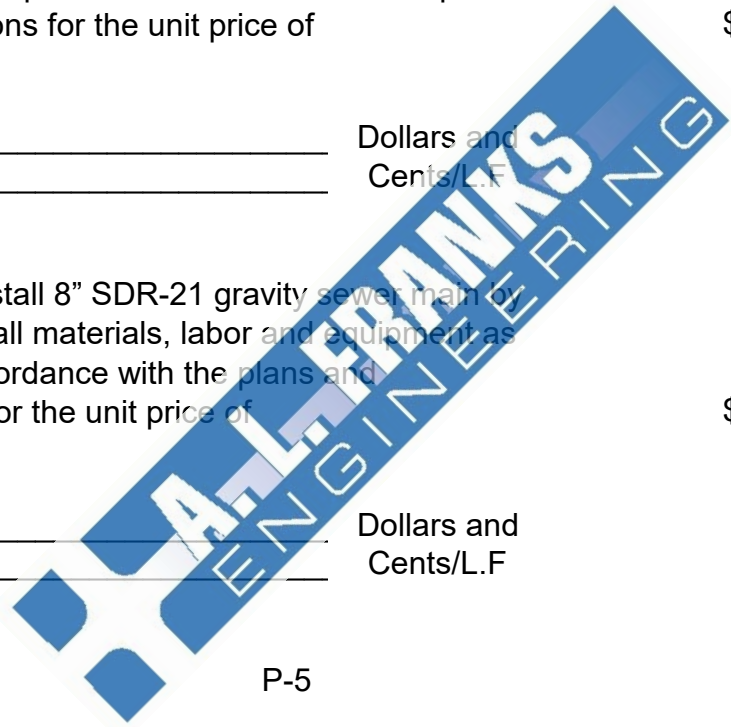


BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
9	60	C.Y.	Provide and install gravel embedment when unfavorable soil conditions are encountered as approved by Engineer including all labor, hauling, materials, compaction, and incidentals required as needed and described in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/C.Y.	\$ _____	\$ _____
10	250	C.Y.	Provide and install compacted select fill where unsuitable fill materials are encountered as approved by Engineer including all labor, hauling, materials, compaction and incidentals required as needed and described in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/C.Y.	\$ _____	\$ _____

BID PROPOSAL CONTINUED


ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
11	1	EA	Provide and install core drill connection to existing manhole as shown in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/EA	\$ _____	\$ _____
12	3	EA	Provide and install connection to existing clay sewer main to proposed manhole as shown in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/EA	\$ _____	\$ _____

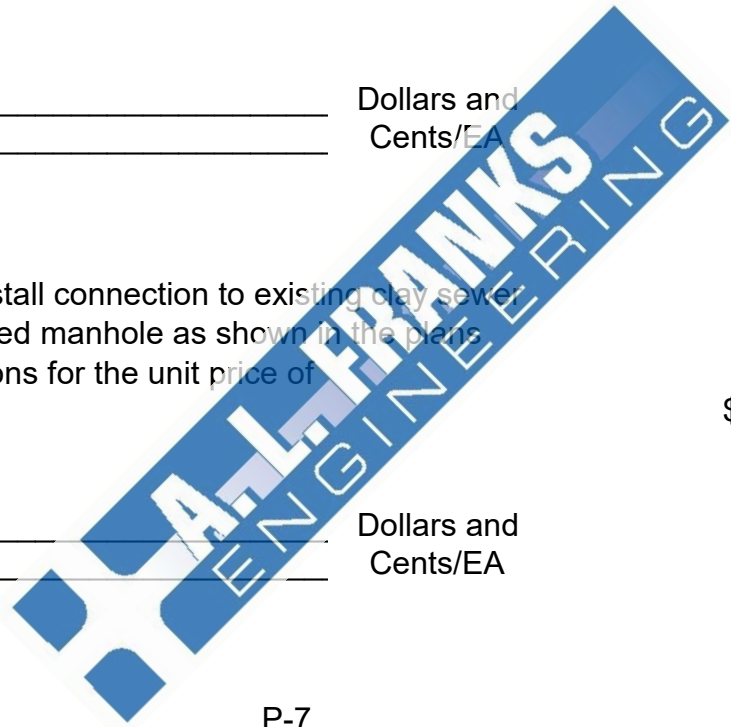

BID PROPOSAL CONTINUED


ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
13	4	EA	Re-connect existing short side sewer service to new main including long side service bore and service line as shown in the plans and specifications for the unit price of	\$ _____	\$ _____
			_____ Dollars and _____ Cents/EA		

14	5	EA	Re-connect existing long side sewer service to new main including long side service bore and service line as shown in the plans and specifications for the unit price of	\$ _____	\$ _____
			_____ Dollars and _____ Cents/EA		

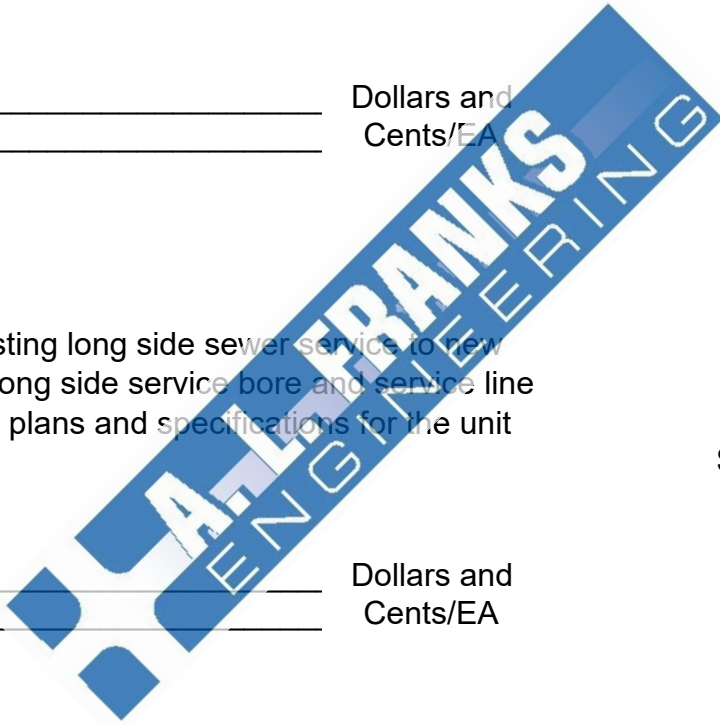

BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
15	2	EA	Provide and install 4-ft diameter concrete manhole with cast iron ring and cover including all labor, material and equipment for the installation as shown in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/EA	\$ _____	\$ _____
16	1	L.S.	Provide and install trench protection as required in accordance with the plans and specifications for the lump sum price of  _____ Dollars and _____ Cents/L.S	\$ _____	\$ _____

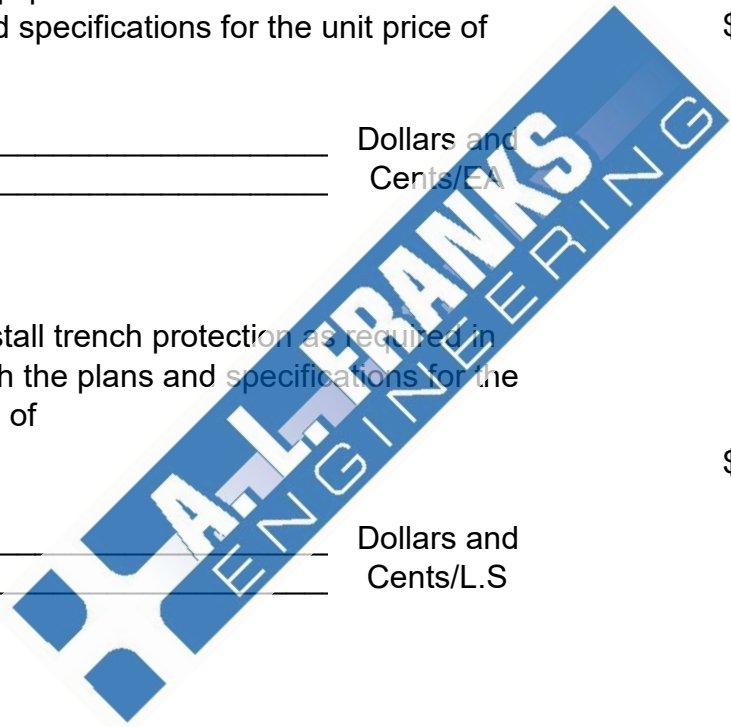




BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
17	1	L.S.	Provide and install erosion control measures as shown on the erosion control plan including silt fencing, seeding, and other controls as necessary to limit erosion throughout the project and establish a minimum of 70% permanent vegetation for the lump sum price of  _____ Dollars and _____ Cents/L.S.	\$ _____	\$ _____
18	0.70	AC	Provide and install hydroseeding at all disturbed areas within the project boundary as necessary to establish permanent vegetation in accordance with ARDOT seeding and fertilizer requirements for site soil type and season for the unit price of  _____ Dollars and _____ Cents/AC	\$ _____	\$ _____

BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
19	1	L.S.	Provide all equipment and materials for Testing Sewer Mains and Manholes per plans and specifications for the lump sum price of	\$ _____	\$ _____
			_____ Dollars and _____ Cents/LS		
20	300	L.F.	Provide and install levee repair including materials, fabric, rock, dewatering, labor, select fill and all other incidental items required per plans and specifications for the unit price of	\$ _____	\$ _____
			_____ Dollars and _____ Cents/L.F.		
<b>TOTAL OF ALL ITEMS (1-20)</b>				\$ _____	



BID PROPOSAL CONTINUED

**NOTES**

Contractor shall submit bids and hold price for a period of no more than 60 days from the bid opening. All work shall be done in accordance with ADEQ, ADH & ARDOT requirements.

Items that are subsidiary to performing the work shall include all labor, equipment, and materials shall be supplied by the contractor. Existing utilities and improvements shall be protected during construction and contractor shall coordinate with City of Keo Utility Department for connections to existing sewer main. Protection measures shall be approved by the engineer prior to construction.

Haul routes approved designated by the city shall be restored to original conditions upon completion of the work. This area is not included in seeding / revegetation and shall be considered subsidiary to the work.

**DEDUCTIVE ALTERNATE #  
DESCRIPTION**


ITEM	QTY	UNIT	DEDUCTIVE ALTERNATE # DESCRIPTION	UNIT PRICE	TOTAL PRICE
1	2	EA	Item #2: <b>REDUCE:</b> Demolition and removal of existing manholes and all associated appurtenances following all applicable ADEQ and ADH guidelines for the removal of manholes for the unit price of	\$ _____	\$ _____

\_\_\_\_\_ Dollars and  
 \_\_\_\_\_ Cents/EA.

BID PROPOSAL CONTINUED

**DEDUCTIVE ALTERNATE #1 CONTINUED  
DESCRIPTION**


<b>ITEM</b>	<b>QTY</b>	<b>UNIT</b>	<b>DESCRIPTION</b>	<b>UNIT PRICE</b>	<b>TOTAL PRICE</b>
2	358	L.F.	Item #3: <b>REDUCE</b> : Abandonment of existing sewer main and all associated appurtenances following all applicable ADEQ and ADH guidelines for the removal of sewer main for the unit price of  _____ Dollars and _____ Cents/L.F.	\$ _____	\$ _____
3	125	S.Y.	Item #4: <b>REDUCE</b> : Removal of existing asphalt pavement to neat lines for the unit price of  _____ Dollars and _____ Cents/S.Y.	\$ _____	\$ _____

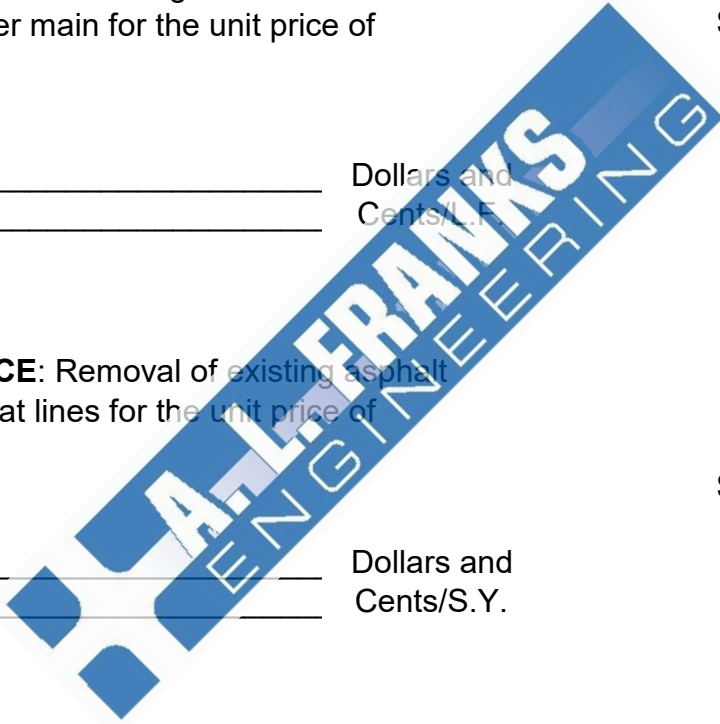

BID PROPOSAL CONTINUED

**DEDUCTIVE ALTERNATE #1 CONTINUED  
DESCRIPTION**


ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
4	1	L.S.	Item #5 <b>REMOVE</b> : Perform removal and replacement of existing stormdrain culverts of various sizes and materials on positive grade including all labor, materials, grading and compaction and as shown in the plans and specifications for the lump sum price of  _____ Dollars and _____ Cents/L.S.	\$ _____	\$ _____
5	125	S.Y.	Item #6: <b>REDUCE</b> : Provide and install asphalt pavement repair as shown in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/S.Y.	\$ _____	\$ _____



BID PROPOSAL CONTINUED

**DEDUCTIVE ALTERNATE #1 CONTINUED  
DESCRIPTION**

<b>ITEM</b>	<b>QTY</b>	<b>UNIT</b>	<b>DESCRIPTION</b>	<b>UNIT PRICE</b>	<b>TOTAL PRICE</b>
6	138	L.S.	Item #7: <b>REDUCE</b> : Provide and install 8" SDR-26 gravity sewer main by open cut including, bedding, all materials, labor and equipment as required in accordance with the plans and specifications for the unit price of  _____ Dollars and _____ Cents/L.S.	\$ _____	\$ _____
7	220	L.S.	Item #8: <b>REDUCE</b> : Provide and install 8" SDR-21 gravity sewer main by bore including all materials, labor and equipment as required in accordance with the plans and specifications for the unit price of  _____ Dollars and _____ Cents/L.S.	\$ _____	\$ _____



BID PROPOSAL CONTINUED

**DEDUCTIVE ALTERNATE #1 CONTINUED**  
**DESCRIPTION**

ITEM	QTY	UNIT	DESCRIPTION	UNIT PRICE	TOTAL PRICE
8	40	C.Y.	Item #9: <b>REDUCE</b> : Provide and install gravel embedment when unfavorable soil conditions are encountered as approved by Engineer including all labor, hauling, materials, compaction, and incidentals required as needed and described in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/C.Y.	\$ _____	\$ _____
9	150	C.Y.	Item #10: <b>REDUCE</b> : Provide and install compacted select fill where unsuitable fill materials are encountered as approved by Engineer including all labor, hauling, materials, compaction and incidentals required as needed and described in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/C.Y.	\$ _____	\$ _____

BID PROPOSAL CONTINUED

**DEDUCTIVE ALTERNATE #1 CONTINUED  
DESCRIPTION**

<b>ITEM</b>	<b>QTY</b>	<b>UNIT</b>	<b>DESCRIPTION</b>	<b>UNIT PRICE</b>	<b>TOTAL PRICE</b>
10	2	EA	Item #12: <b>REDUCE</b> : Provide and install connection to existing clay sewer main to proposed manhole as shown in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/EA.	\$ _____	\$ _____
11	2	EA	Item #13: <b>REDUCE</b> : Re-connect existing short side sewer service to new main including long side service bore and service line as shown in the plans and specifications for the unit price of  _____ Dollars and _____ Cents/EA.	\$ _____	\$ _____



BID PROPOSAL CONTINUED

**DEDUCTIVE ALTERNATE #1 CONTINUED  
DESCRIPTION**

ITEM	QTY	UNIT		UNIT PRICE	TOTAL PRICE
12	3	EA	Item #14: <b>REDUCE:</b> Re-connect existing long side sewer service to new main including long side service bore and service line as shown in the plans and specifications for the unit price of	\$ _____	\$ _____
			_____ Dollars and _____ Cents/EA		
13	1	EA	Item #15: <b>REDUCE:</b> Provide and install 4-ft diameter concrete manhole with cast iron ring and cover including all labor, material and equipment for the installation as shown in the plans and specifications for the unit price of	\$ _____	\$ _____
			_____ Dollars and _____ Cents/EA		
<b>TOTAL DEDUCTIVE ALTERNATE #1</b>				\$ _____	
<b>TOTAL BASE BID LESS ALTERNATE #1</b>				\$ _____	

BID PROPOSAL CONTINUED

ITEM	QTY	UNIT	DEDUCTIVE ALTERNATE #2 DESCRIPTION	UNIT PRICE	TOTAL PRICE
1	300	L.F.	Item #20: <b>REMOVE</b> : Provide and install levee repair including materials, fabric, rock, dewatering, labor, select fill and all other incidental items required per plans and specifications for the unit price of	\$ _____	\$ _____

\_\_\_\_\_ Dollars and  
 \_\_\_\_\_ Cents/L.F.

**TOTAL DEDUCTIVE ALTERNATE #2** \$ \_\_\_\_\_

**TOTAL BASE BID LESS ALTERNATE #2** \$ \_\_\_\_\_

**TOTAL BASE BID LESS ALTERNATE #1 AND ALTERNATE #2** \$ \_\_\_\_\_

